

Bi-weekly Update

Wednesday, May 4, 2022

Progress to date:

As the 2022 construction season continues, the following construction activities have been accomplished during the time-frame of April 20 - May 3, 2022.

- The north bridge berm has been substantially completed.
- Pre-bore and pile driving of six bridge supports on the south side of the project has been completed.
- Two existing bridge girders have been removed during nighttime work, which prepares the structure for placement of load-bearing girders to support the parallel bridge structure.

Two-week look-ahead:

- The retaining wall on the southeast side of the bridge will be completed.
- Pre-bores and pile driving for north bridge supports are planned to be completed.
- Girder placement is planned to be complete with nighttime Interstate closures at LaCrosse Street (Exit 59).

LaCrosse Street
Diverging Diamond
Interchange




Retaining
Wall Under
Construction

Girders
Removed

Utility Replacement Construction
Nearing Ready for Paving

Cranes Staged for Girder Placement and Driving
Abutment Piling

North Bridge Berm Completed

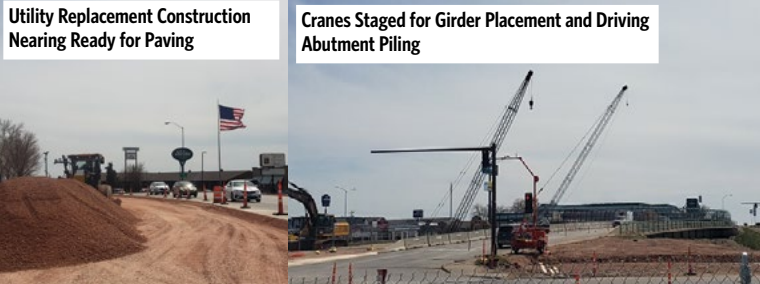

Follow the project progress on social media and
<https://www.i90lacrosseddi.com/construction.html>

