

Bi-weekly Update

Wednesday, June 1, 2022

Progress to date:

As the 2022 construction season continues, the following construction activities have been accomplished during the time-frame of May 18 - May 31, 2022.

- Five girders over the westbound I-90 lanes have been placed.
- Curb and gutter was placed on the southeast side of the bridge and the roadway is prepared for asphalt.
- The retaining wall on the the southeast side of the eastbound I-90 ramp was completed.

Two-week look-ahead:

- Bridge falsework will be constructed to prepare for bridge deck placement on the new structure.
- Asphalt will be placed in areas that have completed curb and gutter.
- Electrical conduit will be placed below grade to connect future street lighting and signals.
- The eastbound LaCrosse Street ramp will be closed for 20 working days (until July 1, 2022) to allow for island construction and placement of stormwater elements.




Eastbound I-90 Ramp to be Closed for 20 Working Days, starting on June 6, 2022



Five Girders Placed over Westbound I-90 Lanes

Retaining Wall Construction on the Southeast Side of LaCrosse Street

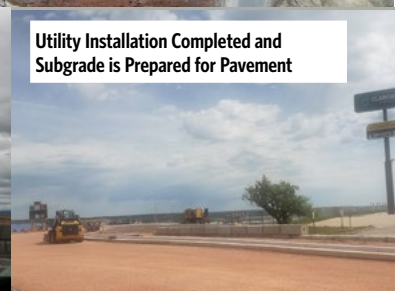

Utility Installation Completed and Subgrade is Prepared for Pavement

Follow the project progress on social media and <https://www.i90lacrosseddi.com/construction.html>

